

Auburn University Construction Project Update June 2010

New Basketball Arena: Construction Cost: \$68.5 million. The Arena achieved the "Substantial Completion" project milestone as of June 4th, 2010. Punch list item work is ongoing. Work related to the project, but not included in the base contract, such as landscaping and Hall of Honor construction is underway and scheduled to be complete later this month. Work has also started on the Team Store inside the common public area.



Southwest View of Arena with Village Housing on the Left



Northeast View of Arena



Southeast View of Arena

Auburn University Construction Project Update June 2010



Practice Gym



Corridor




Courtside Club

Auburn University Construction Project Update June 2010



Courtside Club

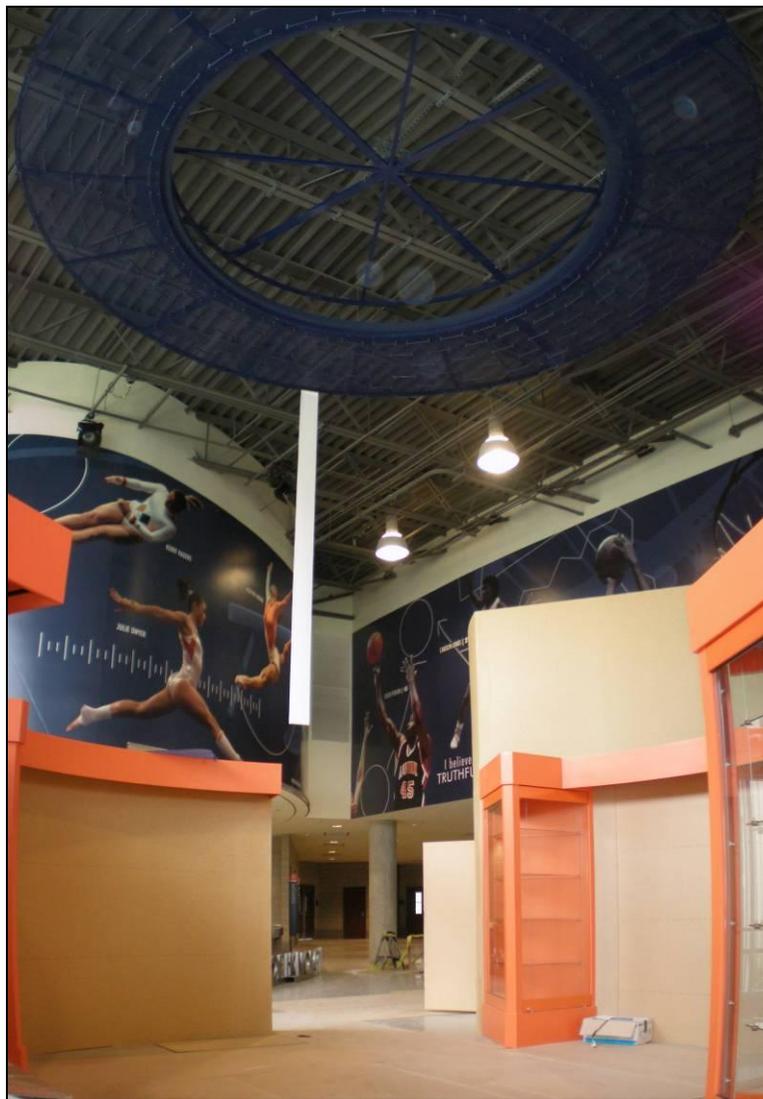

Hall of Honor Area

Auburn University Construction Project Update June 2010



Main Arena Bowl As Seen From Concourse East



Main Arena Bowl As Seen From Concourse North



Men's Locker Room



Men's Players Lounge

Auburn University Construction Project Update

June 2010



Women's Locker Room



Women's Players Lounge



NW Concourse

Auburn University Construction Project Update June 2010

Transportation Technology Center - Phase II: Construction Cost: \$34.0 million. The project is approximately 45% complete and 17 days ahead of schedule. Currently installation of brick veneer and shingle roofing is underway. Project is within budget. Projected completion date: July 2, 2011.



Aerial View Facing North



Aerial View Facing South

Auburn University Construction Project Update

June 2010



Building G Northeast Corner



Building F Northeast Corner



Interior Work

Auburn University Construction Project Update June 2010

District Energy Plant Expansion: Construction cost: \$9.9 million. Substantial completion of the installation of two new 2500 ton chillers inside the existing District Energy plant and construction of two cooling towers was achieved this month. This project will provide additional cooling capacity to the University chilled water system to support the Village Housing complex, Village View Dining facility, and the new Basketball Arena.



New Cooling Tower Enclosures



Existing Plant with New Chillers



Cooling Tower Piping

Auburn University Construction Project Update June 2010

Auburn University Regional Airport Terminal: Construction Cost: \$4.3 million. Currently, the project is 98% complete. Building exterior is 99% complete with interior work consisting of final cleaning and punch list nearing completion. Substantial completion will be in mid-late June.



Interior Views of Terminal Lobby



Airport Terminal--Front



Airport Terminal and Hangar

Auburn University Construction Project Update June 2010

Auburn University Regional Airport Hangar: Construction Cost: \$1.3 million. The project is 98% complete with substantial completion expected to occur this month (mid-June 2010). Metal building is erected and the hangar door installed. Interior finishes (painting, carpet and tile) are progressing well and nearing completion. Next steps will be the final inspections.



AU Hangar Front View—From Taxiway



AU Hanger Back View—From Entrance Road

Auburn University Construction Project Update June 2010

Office of Information Technology (OIT) Building: Construction Cost: \$12.0 million. Project is 38% complete and on schedule. Building site work, foundation construction and installation of underground utilities are complete. Building exterior is progressing well and roof trusses are being installed. Next phase of project is the waterproofing of the exterior and installation of the roof. Project completion date is February 2011.



OIT Building As Seen From Southeast



OIT Building As Seen From West

Auburn University Construction Project Update June 2010



OIT Building as Seen From North



Structural Steel and Building Sheathing



Roof Truss Installation



Interior Work

Auburn University Construction Project Update June 2010

Aquatics Resource Center: Construction Cost: \$6.9 million. Project is 7% complete. Building site grading is in progress and foundations on the first building (administration) are about 40% complete. Next phase of project will be to begin underslab plumbing and electrical piping and start foundations on the second building (laboratory).



Site Work



Site Grading



Foundation Work

Auburn University Construction Project Update June 2010

Campus Green: Construction Cost: \$7 million. Phase II began December 1, 2009 and scope of work involved continuing the brick paver pattern next to the West side of the Stadium, construction of Heisman Drive, pedestrian exit ramps to help with stadium fan egress, sidewalk work, and new electrical and telecommunications panel boxes for television crews. Currently, the project is 98% complete. Paving of the new Duncan Drive is complete and work in the Petrie Bowl Parking area is underway. The project is scheduled to be complete by late July, 2010.



View of the New Heisman Loop Around Shug-Jordan Stadium



View of West Ticket Booth



View of West Pedestrian Concourse

Auburn University Construction Project Update June 2010



Reconfigured Heisman Loop Near Petrie Hall




View of Reconfigured Petrie "Bowl" Parking Area

Auburn University Construction Project Update June 2010

Magnetic Resonance Imaging (MRI) Research Facility: Construction Cost : \$7.6 million with the project currently in budget. The project is approximately 36% complete and tracking on schedule for substantial completion in November 2010. Currently utility work, slab on grade concrete, exterior framing, interior framing, and overhead mechanical & electrical systems are being worked on. The next phase of the project will be the building exterior sheathing, stair installation, roof dry-in, brick veneer work, interior framing and in-wall electrical installation.



View of MRI Research Facility from Devall Dr.

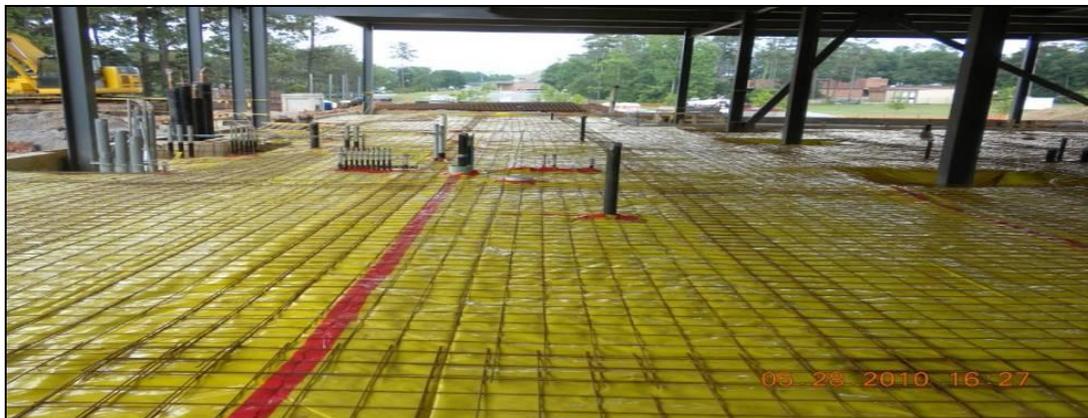

Slab on Grade Concrete Pour Preparations

Auburn University Construction Project Update June 2010

Soccer/Track Facility: Construction Cost: \$4.8 million. Project began in August 2009. Project is nearly 85% complete and a few days behind schedule, however Hardin has committed to maintaining the schedule. Metal roof is complete and the installation of interior sheetrock walls, insulating pipe and ductwork is underway. Exterior brick work is ongoing. The next phase of the project includes installation of windows. Anticipated completion date is the end of July 2010.



Project View from the South (from the Track Side)



Close Up View of Exterior of Soccer/Track Facility
